

NEW PAINT ON ALL GYM WALLS

# LOPEZ ISLAND SCHOOL DISTRICT

Renovation Project  
 Status Update – 1/3/16



NEW DOOR OPENING AT LOBO LAB

### Activities – End of December

- Removed hazard floor tiles and adhesive in all of ES areas and tested & passed all air samples.
- Removed old wall ventilators and patched and painted all walls in library.
- Removed door and patched wall and installed new door at Lobo Lab.
- Installed new wall and floor tiles in ES boys and girls restrooms.

- Painted all HS/MS Gym walls including accent colors.
- Installed new ceilings and light in HS/MS boys and girls restrooms.




NEW PAINT IN LIBRARY

### Activities – Upcoming

- Install plumbing fixtures in ES boys and girls restrooms.
- Frame new walls, hang drywall in ES administration areas.
- Layout and cut slabs for underground plumbing for new ES boys and girls restrooms.

- Continue painting walls in ES all ES areas.
- Begin installation of new bathroom partitions in ES boys and girls restrooms.
- Install rough electric in ES administration areas.
- Install electric trim and new fixtures in ES areas.
- Frame walls and install rough electric in new ES restroom wall.

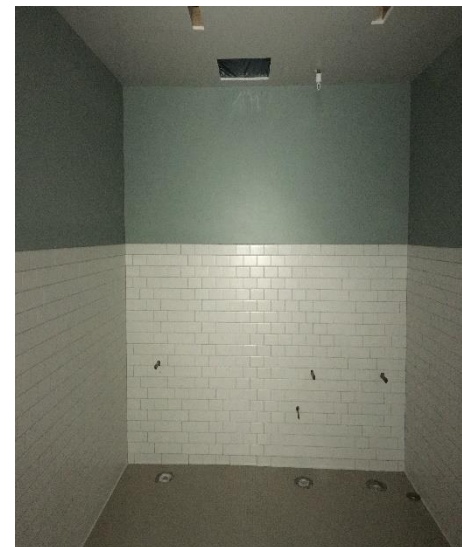

NEW WALL AND FLOOR TILE IN ES RESTROOMS
