



# LOPEZ ISLAND SCHOOL DISTRICT

Renovation Project  
Status Update – 09/06/16



WELCOME BACK TO A NEW FRESH LOOK!!!




COMPLETED REFRESHED CLASSROOMS

## Activities – End of August

- Completion of Phase 1 construction in MS / HS improvements.
- Completion of Phase 1 MS / HS administration offices improvements.
- Completion of MS / HS locker room improvements.
- Partial completion of underground utilities.

- Partial completion of upgraded fire alarm and fire suppression systems.
- Completion of new concrete and gravel walkways.
- Completion of existing septic tank decommissioning / demolition.

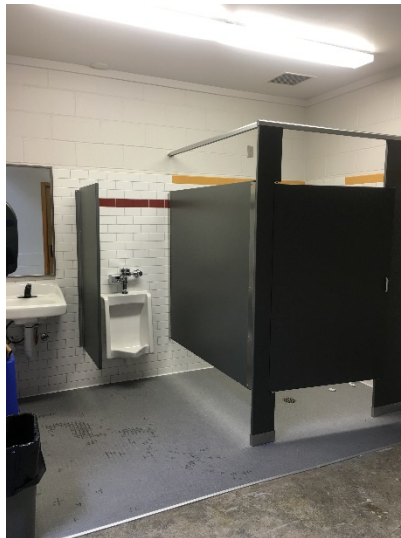


UPDATED LOCKER ROOMS

## Activities – Upcoming

- Continue installation of new septic system.

- Framing and rough-in of electric / plumbing in MS / HS restrooms and Staff Room 13A (Phase 2A work).
- Continue work in Instructional Shop (Phase 2A work).
- Continue demolition in select Elementary classrooms (Phase 2A work).
- Continue work on compressor room and riser room (Phase 2A work).



UPDATED DISTRICT OFFICE



SECURE / PROTECTED AREAS AND SAFETY SIGNAGE

# LOPEZ ISLAND SCHOOL DISTRICT

Renovation Project  
Status Update – 09/06/16



CONTAINED CLASSROOMS

## Phase 2A – Safety Commitment

- Review and pre-planning of Phase 2 work areas.
- Approval of proposed upcoming work areas and flexibility to adjust per safety requirements.
- Install barrier partitions at construction areas to separate construction staff from students.

- Contain construction areas with partition barriers to control dust particulates generated by construction activities.
- Proper use of negative air pressure equipment during demolition.



CONSTRUCTION STAFF WITH PERSONAL PROTECTIVE EQUIPMENT AND IDENTIFICATION BADGES

## Maintaining Safe Work Areas

- Monitor installation of work areas containment per approved plans.

- State-approved background checks for construction staff.
- Construction staff to wear identification badges at all times.
- Coordinate schedule and construction sequencing with District in advance of each phase.
- Conduct Subcontractor and District safety orientation training.
- Coordinate with the District to safely move materials through educational spaces and common areas.



SAFETY SIGNAGE
