



ES POD ATRIUM PREPARING TO ENCLOSE WITH NEW ROOF

# LOPEZ ISLAND SCHOOL DISTRICT

Renovation Project  
 Status Update – 12/13/16




ES NEW DR WALL AND FINISH

## Activities – Beginning Of December

- Removed hazard floor tiles and adhesive in selective areas.
- Removed old flashing in Pod atrium and started installation of new roof to enclose space.
- Continue electrical and plumbing work in ES classrooms 1, 2, boys & girls restrooms and faculty areas.

- Frame new walls, hang drywall and begin finishing for paint.
- Install new barricades and begin work in ES 7 and hallways.
- Continue installing compressor lines in shop for new air compressor.

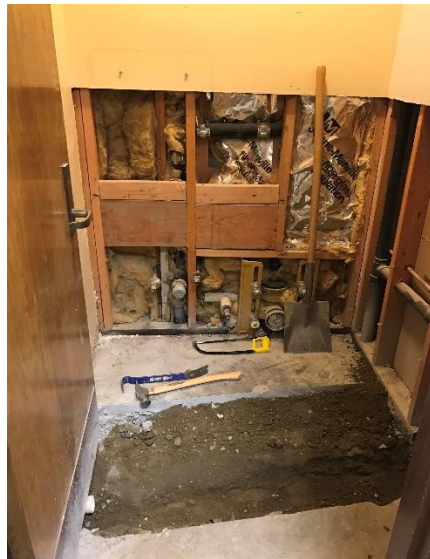

ES NEW PLUMBING AND SANITARY LINES

## Activities – Upcoming

- Remove all remaining hazardous floor tile and adhesive in elementary wing.

- Continue finishing drywall and start priming walls in ES classrooms and faculty area.
- Begin installation of doors hardware and casework in ES classrooms and faculty area.
- Begin installation of ceramic wall and floor tile in ES restrooms.
- Begin demolition in ES administration offices.
- Paint walls in Library and Lobo Lair.



RELOCATE CABINETS IN FACULTY LOUNGE
